



HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter


July 1, 2019 Vol. 15

The HMII3 Project Team is managing the Historic Miramar Infrastructure Improvements Project Phase 3 (HMII3). The intent of this project is to update the 1950's era water mains and enhance fire protection. It will also provide sanitary sewer service that will allow property owners to abandon their septic tank once connected to the new sewer system and improve storm water drainage in your neighborhood.

We encourage you to contact the dedicated HMII3 customer service response team at hmii3@adamsconsulting.biz or 954-998-3146 with questions or for additional information.

What's Taking Place in your Neighborhood?

- Roadway Restoration - (*Light Blue*) construction of curbs on Sunshine Boulevard/SW 68th Way between the cul-de-sac (dead end) and SW 68th Terrace remains in progress. **No parking on curbs on the westside of SW Sunshine Boulevard.**
- Roadway Restoration - (*Light Blue*) construction of roadway grading begins on SW 67th Avenue southbound from Pembroke Road to SW 20th Street and from SW 21st Street to SW 23rd Street and on SW 67th Terrace between SW 21st Street to SW 23rd Street remains in progress.
- Roadway Restoration - (*Light Blue*) – construction of driveways, sprinkler repairs on SW 25th Street between 68th Avenue and 64th Avenue remains in progress. Asphalt driveways were completed June 28, 2019. Reynolds will continue with restoration of smooth paved concrete driveways. Stamped concrete driveways will be restored in the final phase.
- Dewatering remains in progress, and is required until testing is completed. The dewatering equipment is required along SW 25th Street. Weather permitting testing is expected until September 1, 2019.
- Roadway Restoration- (*Light Blue*) construction of the driveways and sidewalks between SW 68th Avenue and Sunshine Boulevard from SW 19th Street to SW 67th Terrace remains in progress. Reynolds Construction will begin constructing asphalt driveways first, followed by paved concrete driveways and finally stamped concrete driveways.
- Sanitary Sewer - (*Green*) construction on SW 20st Street eastbound between SW 66th Avenue and SW 64th Avenue. **No parking on curbsides.**
- Watermain Construction - (*Dark Blue*) lines and Sanitary Sewer - (*Green*) lines are being installed along SW 24th Street, SW 23rd Street and SW 22nd Court between SW 64th Avenue to SW 66th Avenue.
- Watermain Construction - (*Dark Blue*) watermain lines are being constructed on SW 66th Avenue northbound from SW 22nd Street to Pembroke Road remains in progress.

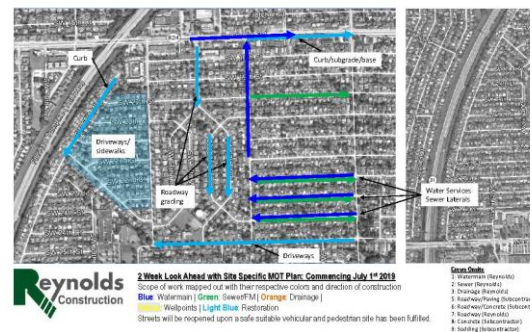

Pembroke Road Business Area – Remains In Progress

Watermain Construction (*Dark Blue*) on Pembroke Road beginning at SW 68th Street going east to SW 64th Avenue will affect the left two eastbound lanes on Pembroke Road. Roadway Restoration - (*Light Blue*) construction of curbs eastbound on Pembroke Road from SW 66th Avenue to SW 64th Avenue remains in progress. **Construction is scheduled from 9 am to 4 pm Monday through Friday and from 9 pm to 5 am Sunday through Thursday.**

Expect delays.

Weather permitting the projected end date for this segment of the project is July 29, 2019.

What's Next?

If you have reported damages to your sprinkler system, driveway or other damages as a result of HMII3 construction, the damages will be repaired by Reynolds Construction. Please contact 954-998-3146 or hmii3@adamsconsulting.biz to report damages.
